

City of Detroit
Dave Bing
Mayor

Detroit City Council

Janice M. Winfrey
City Clerk

Detroit Water and Sewerage
Department

Board of Water Commissioners

Pamela Turner
Director

MACOMB INTERCEPTOR SEWER REPAIRS

PROJECT UPDATE JULY 2009

MAIN REPAIR CONTRACT - (15 Mile and Garfield)

The Detroit Water and Sewerage Department and NTH Consultants have selected Inland Waters Pollution Control as the contractor to perform the Macomb County Sewer System Repairs Project. As of the above date, original project work has been nearly completed (99%) with the only remaining project work consisting of restoring curb and gutter and seeding and mulching on the south side of 15 Mile Road just west of Garfield as well as seeding and mulching for the access shaft on the east side of Garfield Road just north of 15 Mile Road. Traffic barrels are still present on the 15 Mile Road shoulder due to the missing curb and gutter. These sites will be restored in the summer of 2009.


Additional lining repairs to the connection of the 15 Mile Road sewer to the main trunk sewer at the 15 Mile/Garfield Road intersection have begun by installing working platforms. All work will be performed for existing access shafts with only temporary traffic lane shutdowns and Clintondale Pump Station shutdowns. Ventilation activities include a scrubber device at 15 Mile Road and Utica Roads that may cause some odor complaints. This work should be completed by the end of August 2009.

SUPPLEMENTAL REPAIRS

Work has been on going on the Supplemental Repair Contract. In the last several weeks, sewer re-lining has been completed on 18 Mile Road and the bypass pumping system has been removed. Grouting of the main interceptor remains as a work item and should be completed in the next week.

Pavement replacement of Garfield Road just south of 18 Mile Road will be conducted over the next several weeks, which will result in significant traffic restrictions and back-ups. We plan on replacing the pavement sections on Mondays and opening those sections by the end of each week, so no traffic restrictions will be present on the weekends. This work should be completed by the end of August 2009.

DWSD will provide written updates as appropriate throughout the repair period to keep all property and community members fully informed of the progress. Information on project updates and details can be obtained by calling the Project Information Line at 877.329.5858 or on DWSD's Web site at dwsd.org.

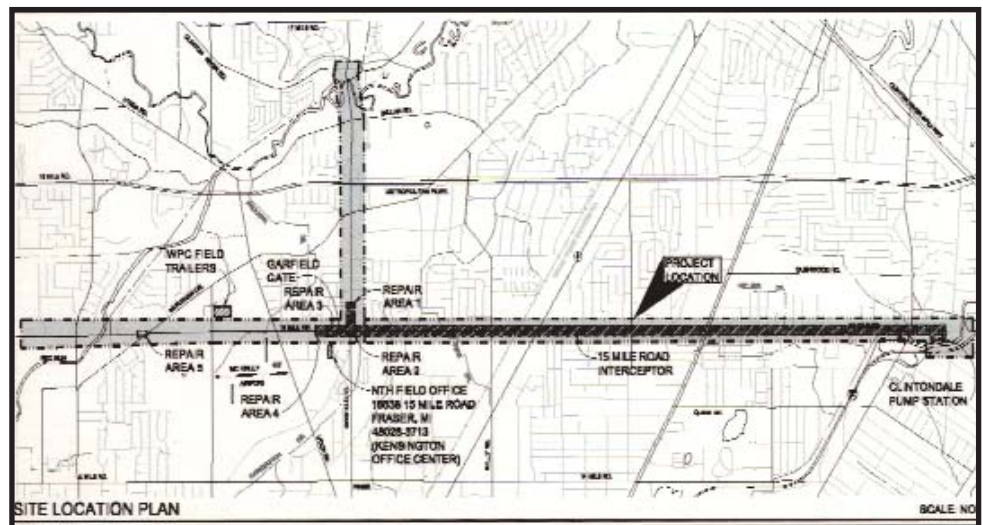

Project Information Line
877.329.5858
or
dwsd.org

facts
