

City of Detroit
Kwame M. Kilpatrick
Mayor

Detroit City Council

Janice M. Winfrey
City Clerk

Detroit Water and Sewerage
Department

Board of Water Commissioners

Victor M. Mercado
Director

MACOMB INTERCEPTOR SEWER REPAIRS

DWSD Sewer Repairs Project Update September 2007

The Detroit Water and Sewerage Department and NTH Consultants have selected Inland Waters Pollution Control as the contractor to perform the Macomb County Sewer System Repairs Project. Substantial completion is scheduled for August 2008.

During the month of September 2007, work was performed in the sewer in the area of Moravian and 15 Mile Road from a manhole on the south side of 15 Mile Road just west of Moravian. Temporary lane closures were utilized on 15 Mile Road at this location. DWSD is currently assessing the need for additional work in this area to perform relining of the sewer. The additional work would add approximately three weeks of occupancy at this location and extend the project schedule by the same amount.


Work in the sewer from the Garfield Gate structure located on the south side of 15 Mile Road just west of Garfield Road is being done utilizing on-going temporary lane closures. Other work in this area consists of removing the eastbound curb lane for a short distance for water main relocation necessary to construct an access shaft into the sewer. Long term closure of the curb lane will be necessary to perform this work.

Construction of a flow control structure in the sewer on Garfield Road just North of 15 Mile Road has begun and will require long term closure of the northbound Garfield Road curb lane.

Work for October will generally occupy the same work locations as September and require no additional lane closures.

Due to the nature of the work, the proposed repairs will be performed mostly during nighttime hours, 7 days per week. The scheduled repairs are anticipated to take 10 months to complete. However, weather will be a factor due to flow conditions inside the sewer. Therefore, the total project duration is an estimate at this time. Currently the project is running approximately one to two weeks ahead of schedule with 30 percent of the required work completed.

DWSD will provide monthly written updates as appropriate throughout the repair period to keep all property and community members fully informed of the progress. Information on project updates and details can be obtained by calling the Project Information Line at 877.329.5858 or on DWSD's website at dwsd.org.

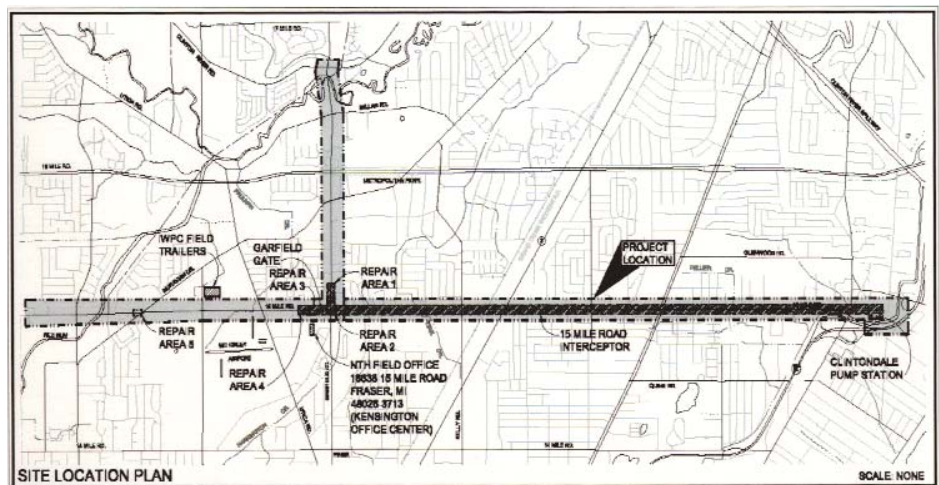

facts

Project Information Line
877.329.5858
or
dwsd.org
