

City of Detroit
 Kwame M. Kilpatrick
 Mayor

Detroit City Council

Janice M. Winfrey
 City Clerk

Detroit Water and Sewerage
 Department

Board of Water Commissioners

Victor M. Mercado
 Director

fast facts

Project Information Line
 877.329.5858
 or
 dwsd.org

MACOMB INTERCEPTOR SEWER REPAIRS PROJECT UPDATE OCTOBER 2007

The Detroit Water and Sewerage Department and NTH Consultants have selected Inland Waters Pollution Control as the contractor to perform the Macomb County Sewer System Repairs Project. The project substantial completion date has been extended for two weeks to allow additional repairs in the Moravian/15 Mile Road area, which are currently being conducted. This extends the project substantial completion date into September 2008. Currently the project is running on that schedule and is 35 percent complete.


During the month of October 2007, work has generally consisted of performing installation of a protective lining inside the sewer surface to restore damaged concrete and prevent future corrosion damage in the area of Moravian and 15 Mile Road from a manhole on the south side of 15 Mile Road just west of Moravian. Temporary lane closures are being performed on 15 Mile Road at that location. Cement work has also been in progress in the sewer from the Garfield Gate Structure located on the south side of 15 Mile Road just west of Garfield Road.

Construction of the large flow control structure into the sewer on Garfield Road just north of 15 Mile Road is on going. Flow control measures to access the sewer have consisted of raising and lowering a steel gate at the Garfield Gate Structure located on the south side of 15 Mile Road just west of Garfield Road in Fraser. Generally, only traffic warning signs have been used at this location. Other flow control consists of shutting down the Clintondale Pumping Station during daylight hours, which does not affect the public.

Work for November will generally consist of completing the additional work at the Moravian location and restoring the area and cementing operations will continue at the Garfield Gate Structure. Temporary lane closures will be on going at both locations. Long-term closure of the Garfield Road northbound curb lane from just north of 15 Mile Road will be on going.

Due to the nature of the work, the proposed repairs will be performed mostly during nighttime hours, 7 days per week. The scheduled repairs are anticipated to take 11 months to complete. However, weather will be a factor due to flow conditions inside the sewer. Therefore, the total project duration is an estimate at this time.

DWSD will provide monthly written updates as appropriate throughout the repair period to keep all property and community members fully informed of the progress. Information on project updates and details can be obtained by calling the Project Information Line at 877.329.5858 or on DWSD's Web site at dwsd.org.

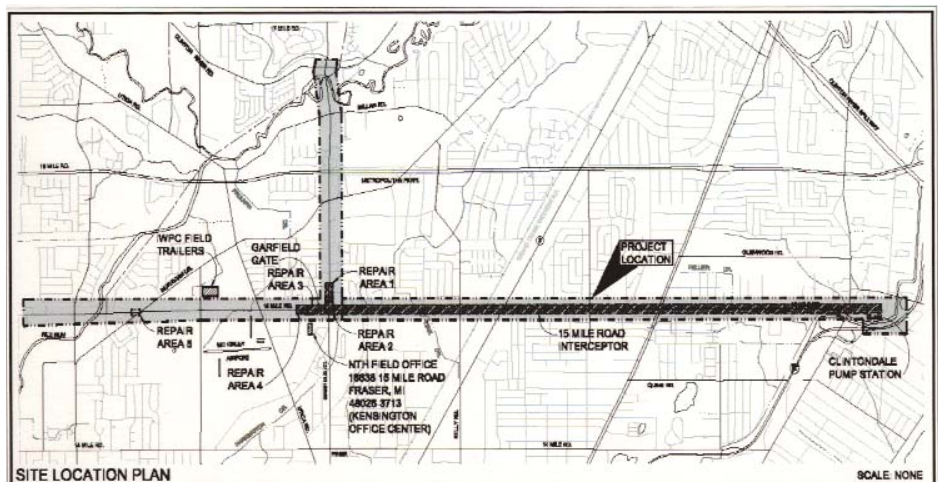

SITE LOCATION PLAN

SCALE NONE
